


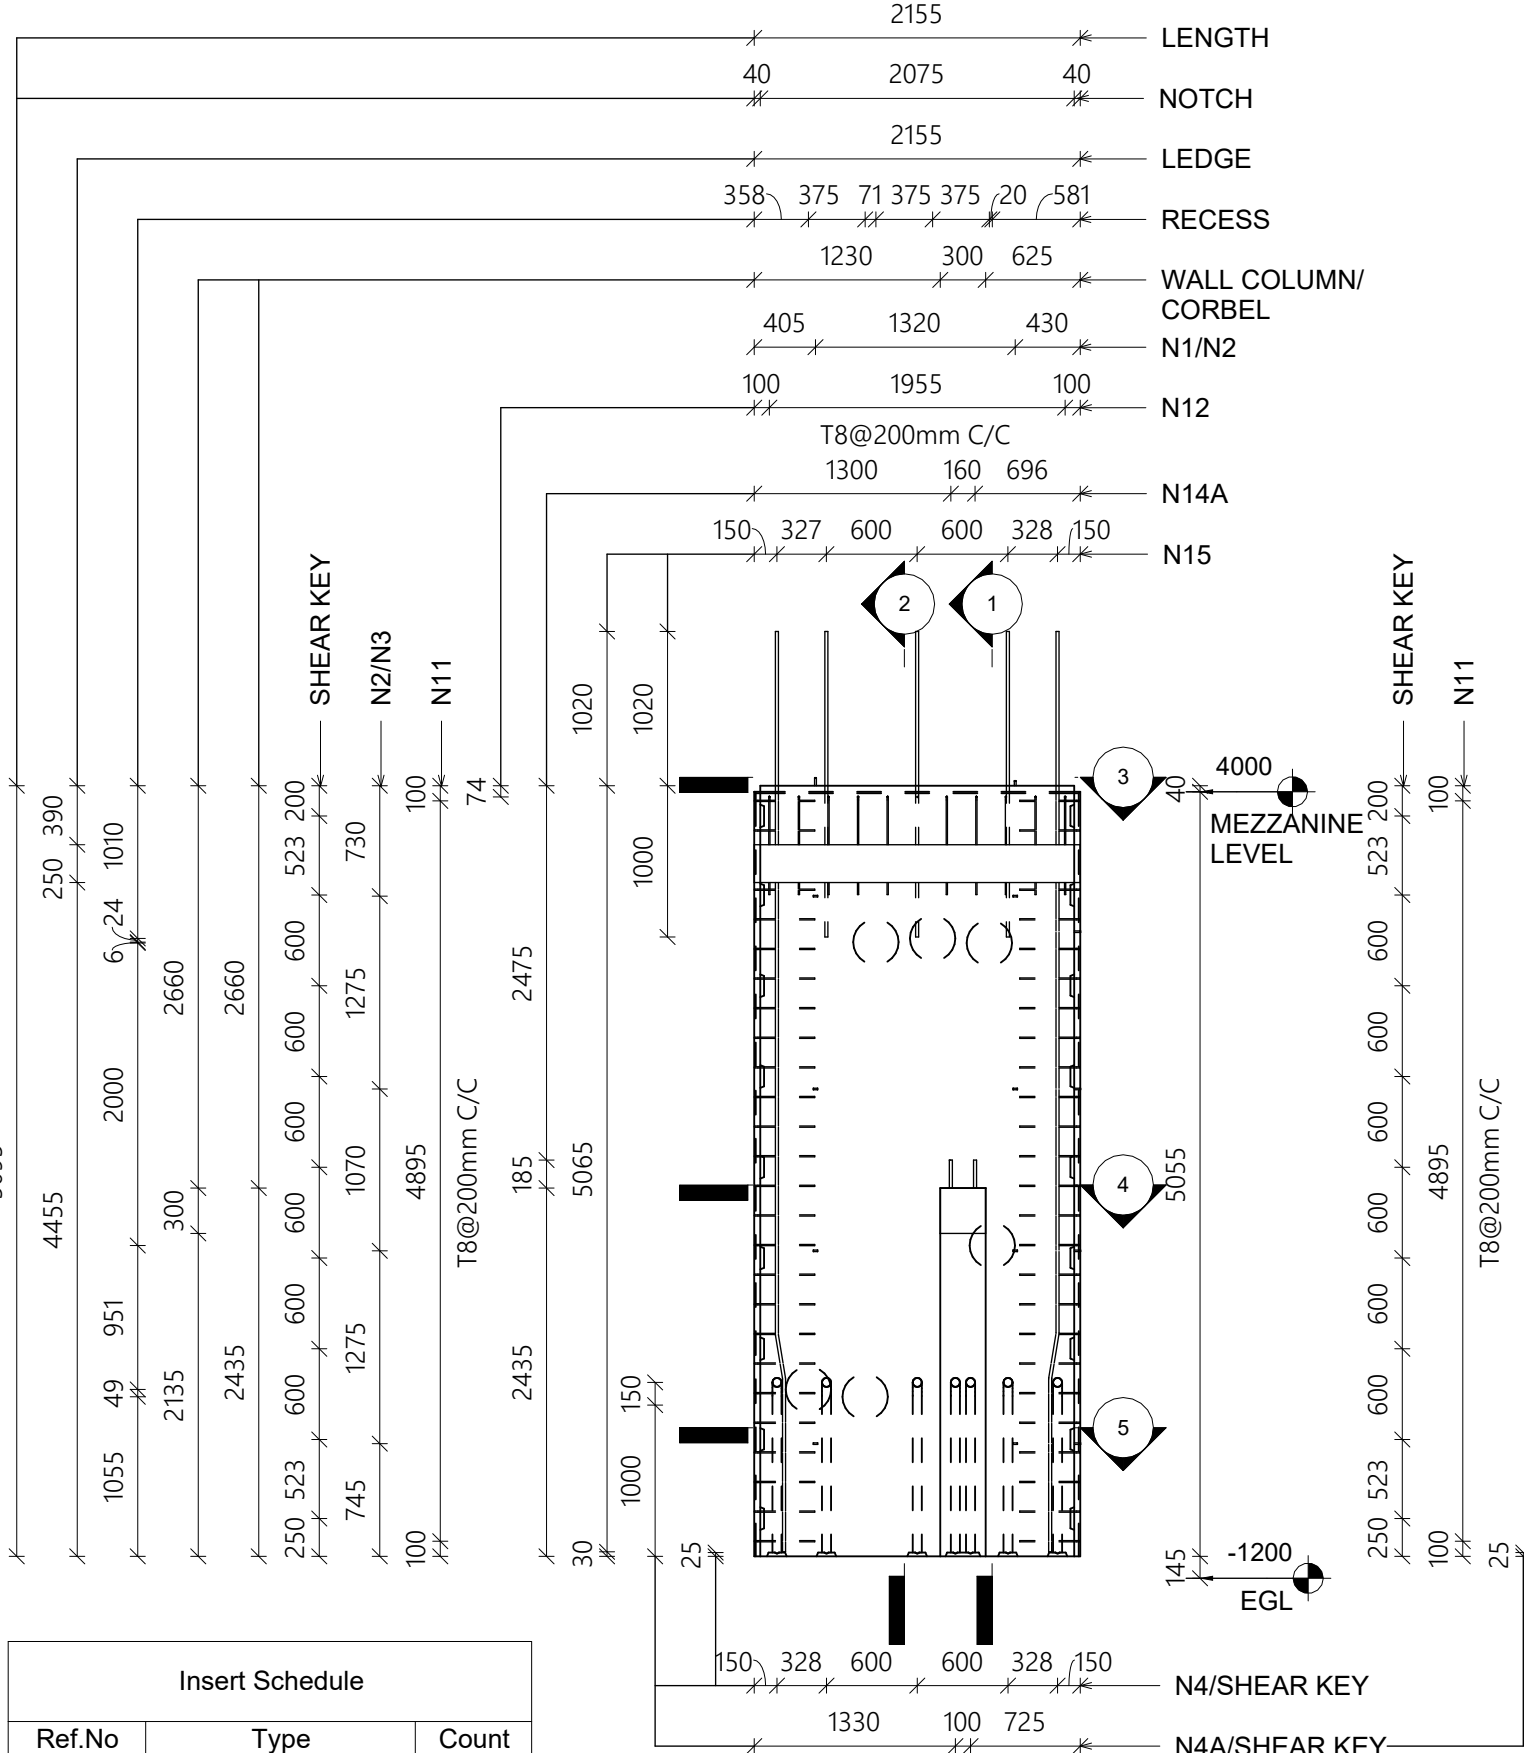

A ELEVATION
1 : 50


Insert Schedule		
Ref.No	Type	Count
N1	RR-SA-4.0-180	2
N2	RR-SA-2.5-200	8
N3	RR-SA-2.5-250	4
N4	60 mm dowel tube	5
N4A	60 mm dowel tube	2

Weight Schedule	
Volume	Weight
2.44 m³	6096.38 kg

Dowel Bar Schedule		
Ref.No	Bar Diameter	Quantity
N14A	20 mm	2
N15	20 mm	5

Loop Bar Schedule		
Ref.No	Bar Diameter	Quantity
N11	8 mm	52

Projecting Bar Schedule		
Ref.No	Bar Diameter	Quantity
N12	8 mm	11

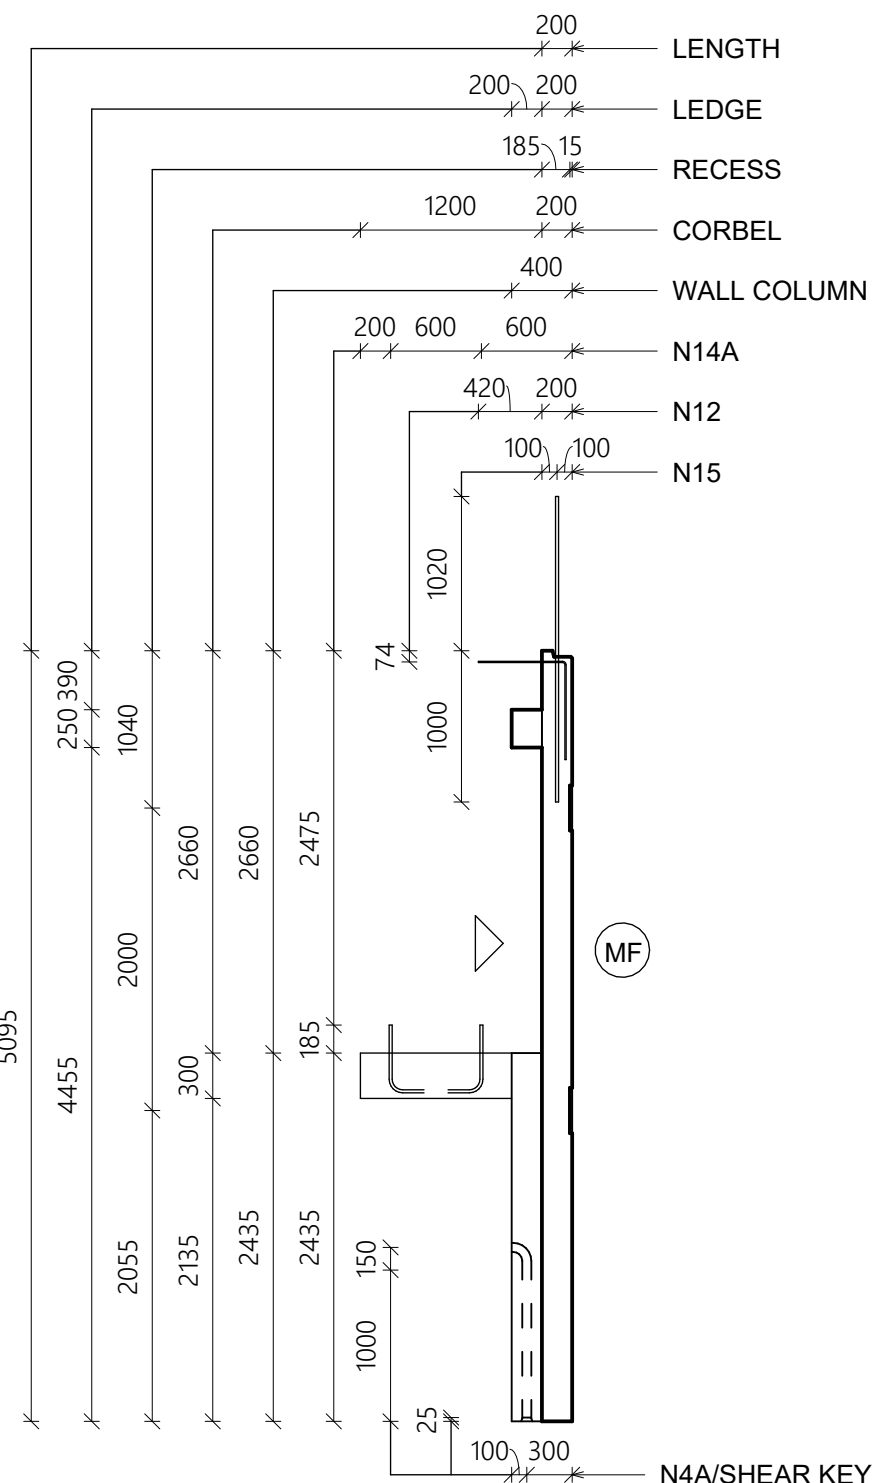

1 SECTION
1 : 50

PROJECT -:
MF FACTORY

- GENERAL NOTES:**
- GRADE OF CONCRETE - M40
 - GRADE OF STEEL - Fe500
 - STRIPPING STRENGTH - M20
- COVER**
- WALL - 30mm
 - CORBEL - 25mm
- ALL DIMENSIONS ARE IN MM

- LEGENDS:**
- ERECTION MARK -
 - MOULD FACE -

CONTRACTOR -:

VME Precast Products

Arihant Esta, 2g2, 2nd floor,
No.370, Church Road, Mogappair East,
Chennai-600037.
Tel:+91- 98400 - 41400 / 90802 - 22066

STRUCTURAL CONSULTANT -:

ES STRUCTURAL CONSULTANT

B167, 12th cross street, Jawahar Nagar,
Palayamkottai, Tirunelveli-627007
Cell No: +91 9865803764

0	14-06-25	FOR APPROVAL	PK	PRC
Rev	Date	Description	Chkd	Appd.

REVISION SCHEDULE

DRAWING TITLE -:
PW-GF-08-MOULD DRAWING

JOB NO. : ESP24075	DRAWN BY:- IH
ELEMENT NO. : PW-GF-08	SHEET SIZE:- A3
DWG. NO. : PW-GF-08(M1)	REV.NO:- 0
SCALE : 1 : 50	LEVEL. :
